


ID	Task Name	Duration	Start	Finish	Predecessors	Successors	May 5, '19				May 12, '19				May 19, '19				Ma	
							W	T	F	S	S	M	T	W	T	F	S	S	M	T
1	<b>PreConstruction Schedule</b>	<b>27 days</b>	<b>Wed 5/1/19</b>	<b>Thu 6/6/19</b>																
2	<b>Long Lead Items</b>	<b>27 days</b>	<b>Wed 5/1/19</b>	<b>Thu 6/6/19</b>																
3	Submittals	5 days	Wed 5/1/19	Tue 5/7/19		5,6,7,8,9,4														
4	Order Structural Wood Trusses	15 days	Wed 5/8/19	Tue 5/28/19	3	11FS-5 days														
5	Order Light Fixtures	22 days	Wed 5/8/19	Thu 6/6/19	3															
6	Order Windows	15 days	Wed 5/8/19	Tue 5/28/19	3															
7	Order Interior Doors / Hardware	10 days	Wed 5/8/19	Tue 5/21/19	3															
8	Order Flooring	10 days	Wed 5/8/19	Tue 5/21/19	3															
9	Order Millwork	15 days	Wed 5/8/19	Tue 5/28/19	3	35														
10	<b>Marand Mobilization / Demolition</b>	<b>3 days</b>	<b>Wed 5/22/19</b>	<b>Fri 5/24/19</b>																
11	Mobilization	3 days	Wed 5/22/19	Fri 5/24/19	4FS-5 days	15SS,28														
12	<b>Construction Schedule</b>	<b>45 days</b>	<b>Wed 5/22/19</b>	<b>Tue 7/23/19</b>																
13	<b>Construction</b>	<b>45 days</b>	<b>Wed 5/22/19</b>	<b>Tue 7/23/19</b>																
14	<b>Exterior Construction</b>	<b>33 days</b>	<b>Wed 5/22/19</b>	<b>Fri 7/5/19</b>																
15	Trim Oak Trees	1 day	Wed 5/22/19	Wed 5/22/19	11SS	16														
16	Demo Exterior	5 days	Thu 5/23/19	Wed 5/29/19	15	17														
17	Pour New Foundations	3 days	Thu 5/30/19	Mon 6/3/19	16	18														
18	Frame New Exterior	10 days	Tue 6/4/19	Mon 6/17/19	17	19														
19	Dry-In Exterior	2 days	Tue 6/18/19	Wed 6/19/19	18	20														
20	Install Roofing / Flashing	3 days	Thu 6/20/19	Mon 6/24/19	19	21														
21	Install Exterior Windows	1 day	Tue 6/25/19	Tue 6/25/19	20	22														
22	Install Exterior Sheathing	2 days	Wed 6/26/19	Thu 6/27/19	21	23														
23	Paint Exterior	4 days	Fri 6/28/19	Wed 7/3/19	22	24														
24	Install Exterior Rails	1 day	Thu 7/4/19	Thu 7/4/19	23	25,56														
25	Punch Out Exterior	1 day	Fri 7/5/19	Fri 7/5/19	24															
26	<b>Interior Construction</b>	<b>43 days</b>	<b>Fri 5/24/19</b>	<b>Tue 7/23/19</b>																
27	<b>Framing / Drywall</b>	<b>5 days</b>	<b>Fri 5/24/19</b>	<b>Thu 5/30/19</b>																
28	Demo Interior Walls/Soffits	1 day	Mon 5/27/19	Mon 5/27/19	11	29,48														
29	Repair / Patch Existing Walls	1 day	Tue 5/28/19	Tue 5/28/19	28	30FS-3 days														
30	Smooth Out Walls	5 days	Fri 5/24/19	Thu 5/30/19	29FS-3 days	32,36,44														
31	<b>Paint</b>	<b>7 days</b>	<b>Fri 5/31/19</b>	<b>Mon 6/10/19</b>																
32	Prime / First Coat	2 days	Fri 5/31/19	Mon 6/3/19	30	41														
33	Final Coat	2 days	Fri 6/7/19	Mon 6/10/19	44,52,53	54														
34	<b>Millwork</b>	<b>5 days</b>	<b>Wed 5/29/19</b>	<b>Tue 6/4/19</b>																
35	Receive Millwork	1 day	Wed 5/29/19	Wed 5/29/19	9	52														
36	Install Millwork	3 days	Fri 5/31/19	Tue 6/4/19	30															
37	<b>Plumbing</b>	<b>3 days</b>	<b>Thu 6/6/19</b>	<b>Mon 6/10/19</b>																
38	Fixtures	2 days	Thu 6/6/19	Fri 6/7/19	52	39														
39	Final Inspection	1 day	Mon 6/10/19	Mon 6/10/19	38															
40	<b>HVAC</b>	<b>2 days</b>	<b>Tue 6/4/19</b>	<b>Wed 6/5/19</b>																
41	HVAC Trim	1 day	Tue 6/4/19	Tue 6/4/19	32	42,54														
42	Final Inspection	1 day	Wed 6/5/19	Wed 6/5/19	41															



ID	Task Name	Duration	Start	Finish	Predecessors	Successors	May 5, '19				May 12, '19				May 19, '19				Ma		
							W	T	F	S	S	M	T	W	T	F	S	S	M	T	W
43	<b>Electrical</b>	<b>9 days</b>	<b>Tue 5/28/19</b>	<b>Fri 6/7/19</b>																	
44	Install Light Fixtures	3 days	Fri 5/31/19	Tue 6/4/19	30	33,45															
45	Electrical Trim Out	1 day	Wed 6/5/19	Wed 6/5/19	44	46,54															
46	Inspection	1 day	Thu 6/6/19	Thu 6/6/19	45																
47	<b>Low Voltage Wiring</b>	<b>9 days</b>	<b>Tue 5/28/19</b>	<b>Fri 6/7/19</b>																	
48	Pull low voltage wire	3 days	Tue 5/28/19	Thu 5/30/19	28	49															
49	Terminate low voltage wire	3 days	Fri 5/31/19	Tue 6/4/19	48	50															
50	Security	3 days	Wed 6/5/19	Fri 6/7/19	49																
51	<b>Flooring</b>	<b>10 days</b>	<b>Thu 5/30/19</b>	<b>Wed 6/12/19</b>																	
52	Install CT	5 days	Thu 5/30/19	Wed 6/5/19	35	53,38,33															
53	Install LVT	1 day	Thu 6/6/19	Thu 6/6/19	52	33															
54	Install Carpet	2 days	Tue 6/11/19	Wed 6/12/19	33,41,45	56															
55	<b>Closeout</b>	<b>12 days</b>	<b>Fri 7/5/19</b>	<b>Mon 7/22/19</b>																	
56	Marand Punch	5 days	Fri 7/5/19	Thu 7/11/19	54,24	59,58,57															
57	Owner Punch	5 days	Fri 7/12/19	Thu 7/18/19	56	59,58															
58	Final Punch	1 day	Fri 7/19/19	Fri 7/19/19	56,57	59															
59	Turn Over to Owner	1 day	Mon 7/22/19	Mon 7/22/19	56,57,58	61															
60	<b>Construction Complete Date</b>	<b>1 day</b>	<b>Tue 7/23/19</b>	<b>Tue 7/23/19</b>																	
61	Construction Completed	1 day	Tue 7/23/19	Tue 7/23/19	59																

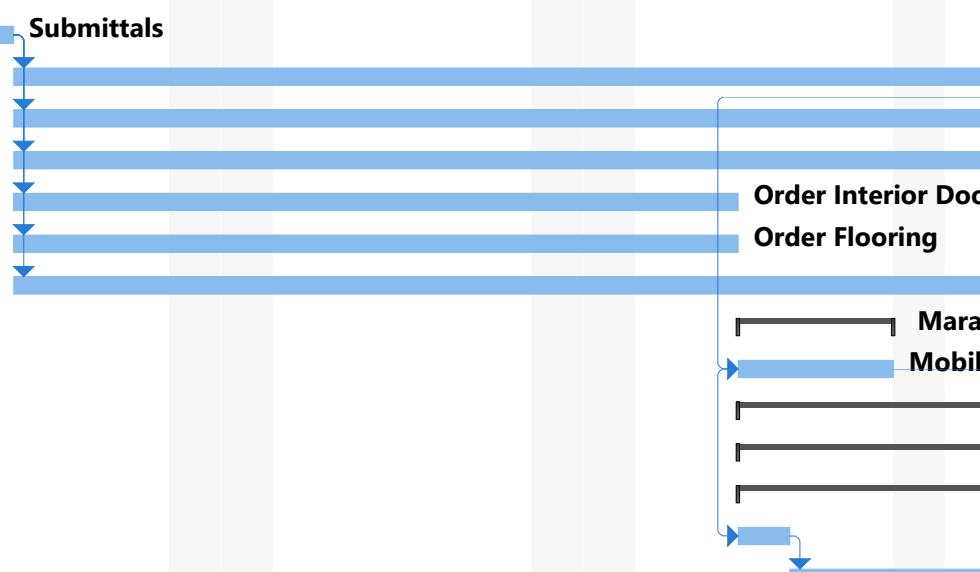
